


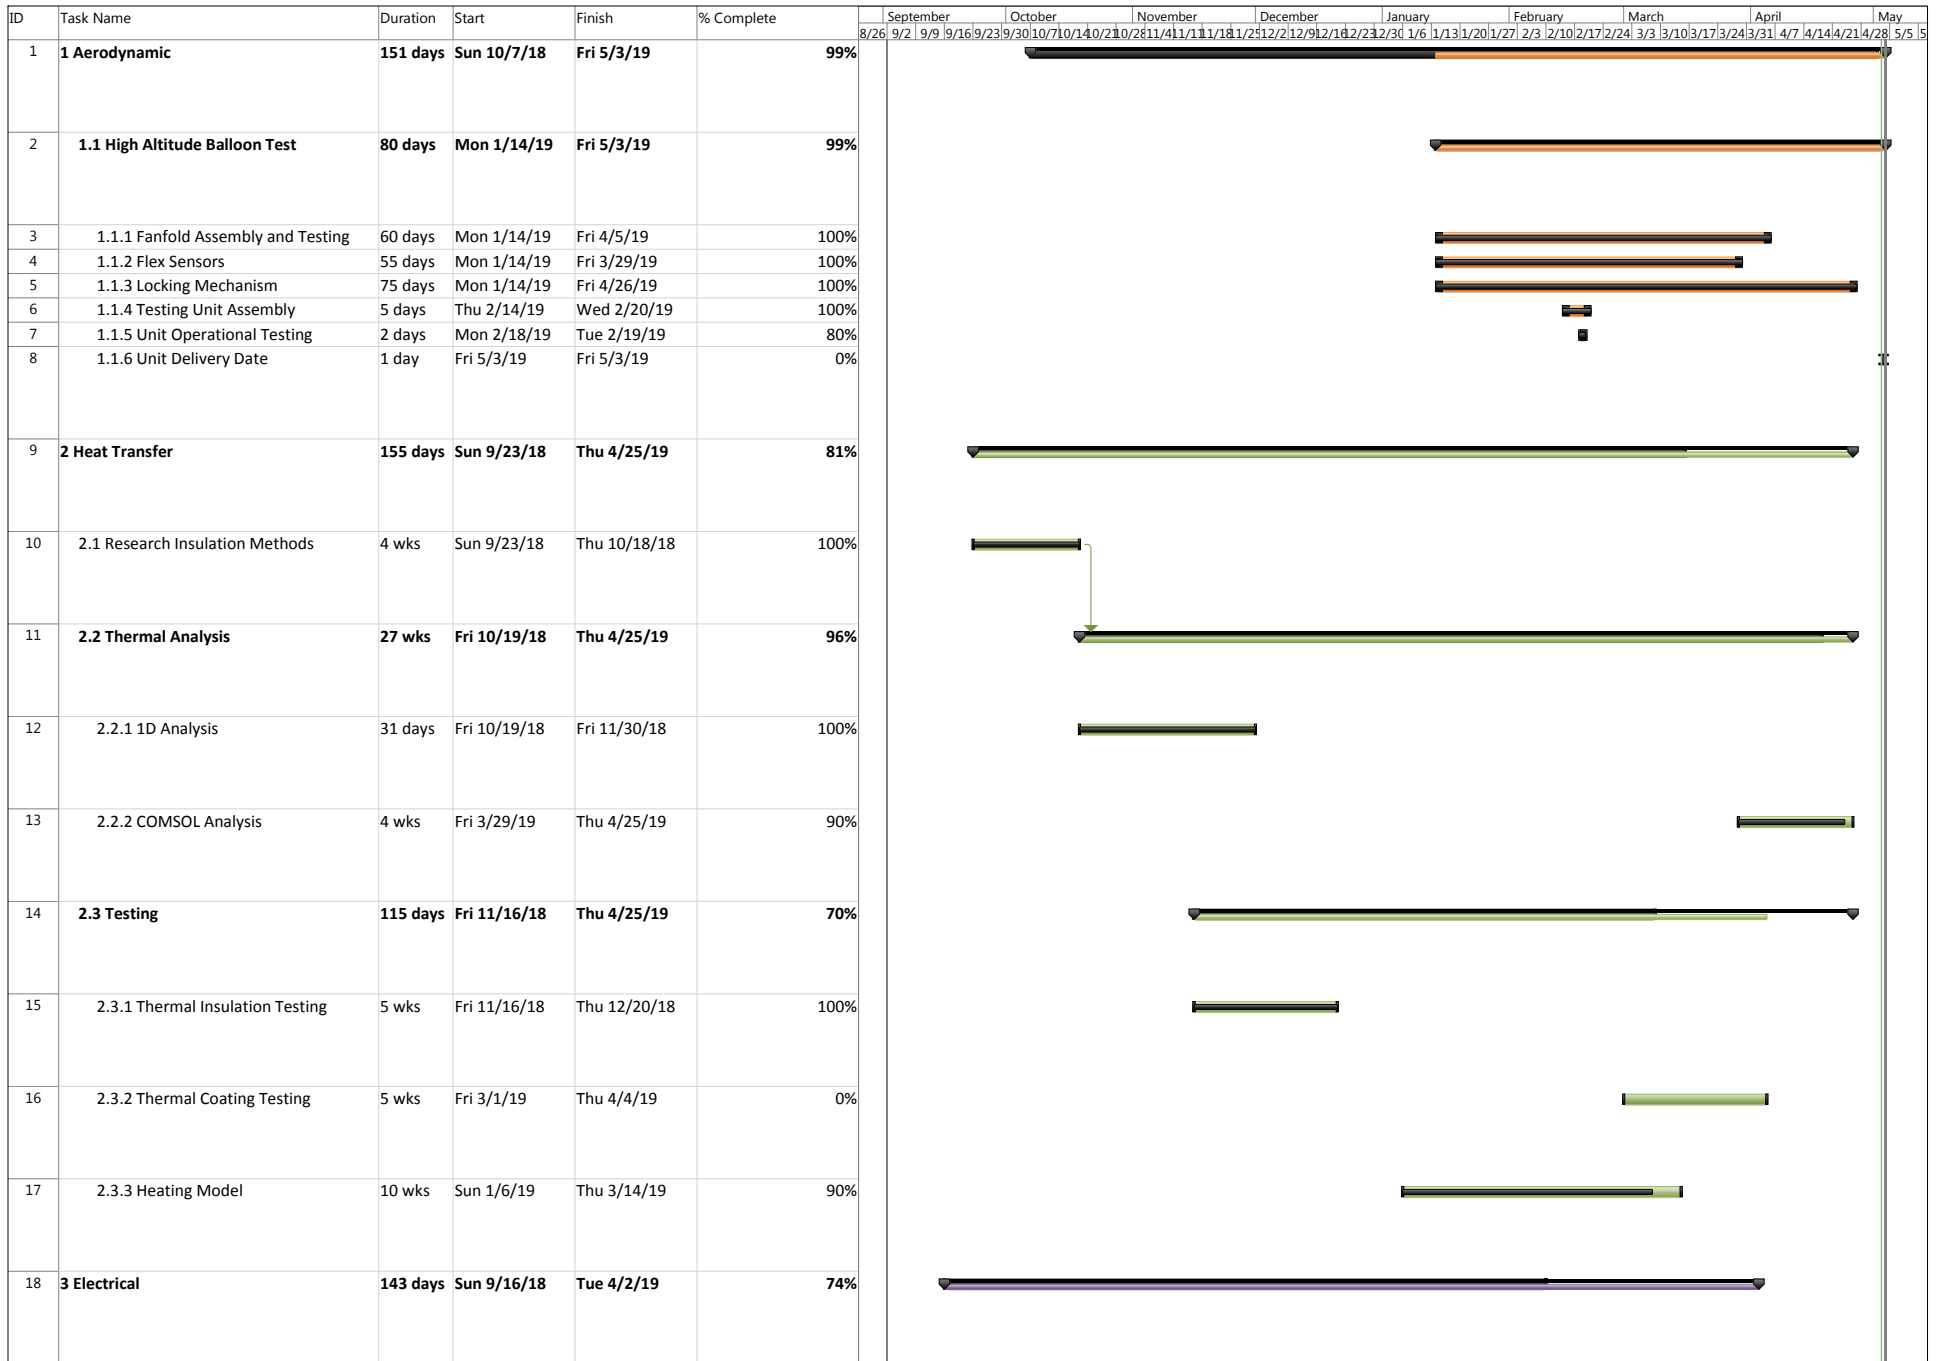

ID	Task Name	Duration	Start	Finish	% Complete																												
						September	October	November	December	January	February	March	April	May																			
19	3.1 ThermoElectric Research	23.2 wks	Sun 9/16/18	Fri 2/22/19	70%																												
20	3.2 Payload	58 days	Sun 1/13/19	Tue 4/2/19	80%																												
21	3.2.1 High Altitude Balloon Test Code	18 days	Wed 2/6/19	Fri 3/1/19	100%																												
22	3.2.2 Updating of Arduino Code	8.2 wks	Sun 1/13/19	Fri 3/8/19	60%																												
23	3.2.3 Design Payload Layout	1.2 wks	Mon 2/25/19	Mon 3/4/19	100%																												
24	3.2.4 Test operation	15 days	Wed 3/13/19	Tue 4/2/19	100%																												
25	4 Outreach	160 days	Sun 9/16/18	Thu 4/25/19	95%																												
26	4.1 Create Teaching instructions	14 wks	Sun 9/16/18	Thu 12/20/18	100%																												
27	4.2 X-Chip	5 wks	Sun 9/16/18	Thu 10/18/18	100%																												
28	4.3 Phase 1A Documentation	6 wks	Sun 9/30/18	Thu 11/8/18	100%																												
29	4.4 Dashboard User Guide	10 days	Mon 2/4/19	Fri 2/15/19	100%																												
30	4.5 Low Altitude Balloon Test	80 days	Fri 11/9/18	Thu 2/28/19	100%																												
31	4.5.1 FlatSat Experiment	12 wks	Fri 11/9/18	Thu 1/31/19	100%																												
32	4.5.2 Design Low Altitude Balloon Test	3 wks	Sun 1/6/19	Thu 1/24/19	100%																												
33	4.5.3 Balloon Experiment	5 wks	Fri 1/25/19	Thu 2/28/19	100%																												
34	4.6 Data Analysis Tools	25.2 wks	Thu 11/1/18	Thu 4/25/19	80%																												
35	4.7 Elementry School Experiments	54 days	Mon 2/11/19	Thu 4/25/19	100%																												
36	4.8 Website	59 days	Mon 2/4/19	Thu 4/25/19	100%																												
